

## Site HOTO Report — SYL\_X0089

Project Tiger · Dhaly Infratech → Alliance Computers Limited · Generated 07-Sep-2026 20:53 BD time

**100%**

FORM COMPLETION

**14/15**

CHECKLIST OK

**1**

OPEN SNAGS

**1**

TOTAL SNAGS

**8**

PHOTOS ATTACHED

### SITE & HANDOVER DETAILS

|                        |                 |                      |                            |
|------------------------|-----------------|----------------------|----------------------------|
| SITE CODE              | SYL_X0089       | ZONE                 | Sylhet                     |
| HOTO DATE              | 2026-09-01      | DISTRICT             | Sunamganj                  |
| HANDOVER ORG           | Dhaly Infratech | TAKEOVER ORG         | Alliance Computers Limited |
| HANDOVER PERSON        | Md. Anwar       | TAKEOVER PERSON      | Md. Ismail Hossain         |
| HANDOVER PHONE         | 01734713807     | TAKEOVER PHONE       | 01847426858                |
| INSPECTED BY           | Ismail Siraji   | SECURITY GUARD       | Yes                        |
| ACCESS KEY HANDED OVER | Yes             | SITE TYPE            | GFT                        |
| BTS TYPE               | Outdoor         |                      |                            |
| SHARED WITH OPERATOR   | No              | SHARED OPERATOR NAME | N/A                        |


### GENERATOR INFORMATION

|                        |                         |                           |                         |
|------------------------|-------------------------|---------------------------|-------------------------|
| DG BRAND               | Tempest                 | GENSET ASSET NO.          | N/A                     |
| CAPACITY (KVA)         | 20                      | TYPE                      | Can                     |
| FUEL TANK CAPACITY     | 2000                    | PRESENT RH                | 2241                    |
| FUEL (NO WATER)        | 104 L                   | FUEL (TOTAL)              | 104 L                   |
| WATER AMOUNT           | — L                     | FUEL AMOUNT (WORD)        | One hundred four litter |
| DG SITE TYPE           | Remote                  | DG LOCKED AFTER FUELING   | Yes                     |
| DG PRESENT STATUS      | OK                      | GENSET ON ALARM           | OK                      |
| BATTERY BRAND          | Hamko                   | BATTERY SERIAL            | P033XEBD0616            |
| BATTERY AH             | 100                     | ENGINE SERIAL             | GN66044U                |
| ATS BRAND              | Local                   | ATS MODE                  | Auto                    |
| RH METER TYPE          | Digital from controller | LAST SERVICE DATE         | 2026-04-30              |
| KEY TYPE               | Local Key               | KEY STATUS — BTS          | Local                   |
| KEY STATUS — DG ROOM   | Local                   |                           |                         |
| ACTIVE DG              | 1                       | CONNECTED FUEL TANKS      | 1                       |
| FAULTY/DISCONNECTED DG | —                       | FAULTY/DISCONNECTED TANKS | —                       |

## CONNECTED GENERATOR CHECKLIST & READINGS

| ITEM                                                 | VALUE | ITEM                                          | VALUE    |
|------------------------------------------------------|-------|-----------------------------------------------|----------|
| Earth Connection OK                                  | Yes   | Load Current (A)                              | 34       |
| Frequency (Hz)                                       | 51    | Phase                                         | 3 Phase  |
| Output                                               | 410   | Engine Brand                                  | Parkings |
| Voltage L1-L2                                        | 410   | Voltage L2-L3                                 | 410      |
| Voltage L3-L1                                        | 409   | Voltage L1-N                                  | 235      |
| Voltage L2-N                                         | 235   | Voltage L3-N                                  | 234      |
| Current Line 1                                       | 11    | Current Line 2                                | 12       |
| Current Line 3                                       | 11    | N-G                                           | 0.047    |
| Controller Status                                    | OK    | Black Smoke Status                            | OK       |
| DG Battery Charger                                   | OK    | ATS Physical & Functional Status              | OK       |
| DG Automation (VDTC/RVDTC/Rectifier) per BL Standard | OK    | Fuel Preserved at Safe & Appropriate Location | OK       |
| Exhaust Fan / Ventilation Sufficient When Running    | OK    | Sufficient Water in Radiator & Battery        | OK       |
| DG Radiator Condition                                | OK    | DG Battery Condition                          | OK       |
| DG Runs in Both Auto & Manual Mode                   | OK    | GENSET ON Alarm Functioning Properly          | OK       |
| Lub Oil Status (Level & Colour)                      | NOK   | DG RH Meter Working Properly                  | OK       |
| No Parts Missing (if missing, note in snags below)   | OK    |                                               |          |


## SNAGS FOUND (1)

| SNAG # | SYSTEM | CATEGORY   | COMPONENT | STATUS | OBSERVATIONS | ACTION | PHOTO                                                                                 |
|--------|--------|------------|-----------|--------|--------------|--------|---------------------------------------------------------------------------------------|
| S-008  | DG     | DG - Other | Over Run  | Faulty | —            | Open   |  |

## DEFICIENCIES & SAFETY REMARKS

|                       |                   |
|-----------------------|-------------------|
| DG MAJOR DEFICIENCIES | Need to servicing |
| SAFETY REMARKS        | Need to servicing |
| GENERAL REMARKS       | Need to servicing |

## SITE PHOTOS

|                                                                                                         |                                                                                                      |                                                                                                    |
|---------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------|
| <br>Site / Nameplate | <br>DG RH / Meter | <br>Fuel Gauge |
|---------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------|



Additional



Additional



Additional



Additional

---

**Md. Anwar**

Handed Over By · Dhaly Infratech  
01734713807

Date: \_\_\_\_\_

---

**Md. Ismail Hossain**

Taken Over By · Alliance Computers  
Limited

01847426858

Date: \_\_\_\_\_

---

BL Concern · Name / Signature

Date: \_\_\_\_\_


## APPENDIX — PHOTO EVIDENCE (8)

Full-size reference photos for SYL\_X0089, grouped by type and numbered for cross-reference against the tables above.

### REQUIRED SITE PHOTOS (3)



**Photo 1 — Site / Nameplate**

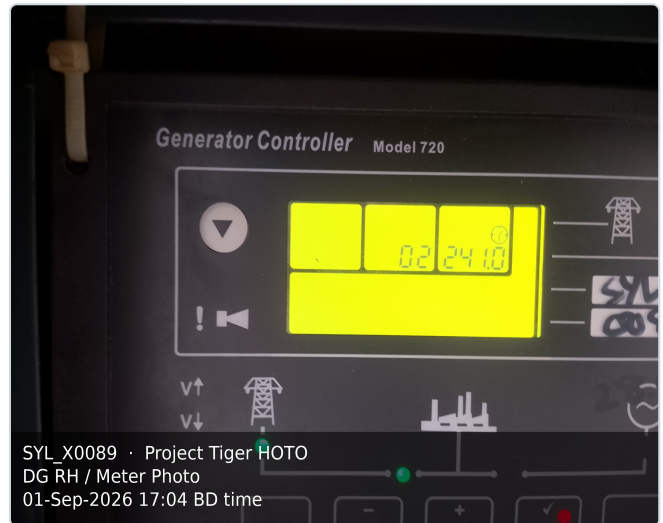

**Photo 2 — DG RH / Meter**



**Photo 3 — Fuel Gauge**

## SNAG EVIDENCE PHOTOS (1)

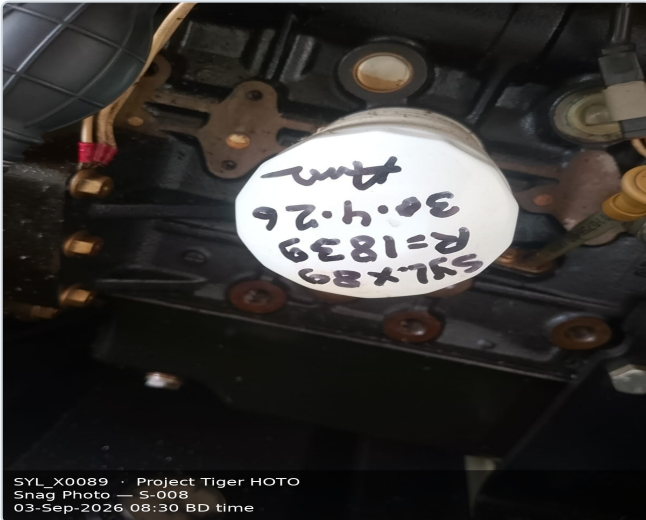


Photo 4 — S-008 — Over Run

## ADDITIONAL PHOTOS (4)



Photo 5 — Site Context 1



Photo 6 — Site Context 2



Photo 7 — Site Context 3



Photo 8 — Site Context 4
