

## Site HOTO Report — SYL\_X0086

Project Tiger · Dhaly Infratech → Alliance Computers Limited · Generated 07-Sep-2026 20:23 BD time

**100%**

FORM COMPLETION

**14/15**

CHECKLIST OK

**2**

OPEN SNAGS

**2**

TOTAL SNAGS

**5**

PHOTOS ATTACHED

### SITE & HANDOVER DETAILS

|                        |                 |                      |                            |
|------------------------|-----------------|----------------------|----------------------------|
| SITE CODE              | SYL_X0086       | ZONE                 | Sylhet                     |
| HOTO DATE              | 2026-09-02      | DISTRICT             | Sunamganj                  |
| HANDOVER ORG           | Dhaly Infratech | TAKEOVER ORG         | Alliance Computers Limited |
| HANDOVER PERSON        | Md. Eidris Ali  | TAKEOVER PERSON      | Md. Ismail Hossain         |
| HANDOVER PHONE         | 01750537433     | TAKEOVER PHONE       | 01847426858                |
| INSPECTED BY           | Ismail Siraji   | SECURITY GUARD       | Yes                        |
| ACCESS KEY HANDED OVER | Yes             | SITE TYPE            | GFT                        |
| BTS TYPE               | Outdoor         |                      |                            |
| SHARED WITH OPERATOR   | Yes             | SHARED OPERATOR NAME | Robi                       |

### GENERATOR INFORMATION


|                      |                         |                         |                                 |
|----------------------|-------------------------|-------------------------|---------------------------------|
| DG BRAND             | FG Wilson               | GENSET ASSET NO.        | N/A                             |
| CAPACITY (KVA)       | 22                      | TYPE                    | Can                             |
| FUEL TANK CAPACITY   | 850                     | PRESENT RH              | 341.5                           |
| FUEL (NO WATER)      | 163 L                   | FUEL (TOTAL)            | 179 L                           |
| WATER AMOUNT         | 16 L                    | FUEL AMOUNT (WORD)      | One Hundred Seventy Nine Liters |
| DG SITE TYPE         | Standard                | DG LOCKED AFTER FUELING | Yes                             |
| DG PRESENT STATUS    | OK                      | GENSET ON ALARM         | OK                              |
| BATTERY BRAND        | Lucas                   | BATTERY SERIAL          | 3AI5VY12787359                  |
| BATTERY AH           | 100                     | ENGINE SERIAL           | HP51109V983311P                 |
| ATS BRAND            | Local                   | ATS MODE                | Auto                            |
| RH METER TYPE        | Digital from controller | LAST SERVICE DATE       | 2026-07-31                      |
| KEY TYPE             | Local Key               | KEY STATUS — BTS        | 00                              |
| KEY STATUS — DG ROOM | Open                    |                         |                                 |
| ACTIVE DG            | 1                       | CONNECTED FUEL TANKS    | 1                               |

|                        |   |                           |   |
|------------------------|---|---------------------------|---|
| FAULTY/DISCONNECTED DG | — | FAULTY/DISCONNECTED TANKS | — |
|------------------------|---|---------------------------|---|

### CONNECTED GENERATOR CHECKLIST & READINGS

| ITEM                                                 | VALUE | ITEM                                          | VALUE    |
|------------------------------------------------------|-------|-----------------------------------------------|----------|
| Earth Connection OK                                  | Yes   | Load Current (A)                              | 42       |
| Frequency (Hz)                                       | 48.8  | Phase                                         | 3 Phase  |
| Output                                               | 401   | Engine Brand                                  | Parkingd |
| Voltage L1-L2                                        | 401   | Voltage L2-L3                                 | 402      |
| Voltage L3-L1                                        | 402   | Voltage L1-N                                  | 230      |
| Voltage L2-N                                         | 231   | Voltage L3-N                                  | 231      |
| Current Line 1                                       | 14    | Current Line 2                                | 14       |
| Current Line 3                                       | 14    | N-G                                           | 1.86     |
| Controller Status                                    | OK    | Black Smoke Status                            | OK       |
| DG Battery Charger                                   | OK    | ATS Physical & Functional Status              | OK       |
| DG Automation (VDTC/RVDTC/Rectifier) per BL Standard | OK    | Fuel Preserved at Safe & Appropriate Location | OK       |
| Exhaust Fan / Ventilation Sufficient When Running    | OK    | Sufficient Water in Radiator & Battery        | OK       |
| DG Radiator Condition                                | NOK   | DG Battery Condition                          | OK       |
| DG Runs in Both Auto & Manual Mode                   | OK    | GENSET ON Alarm Functioning Properly          | OK       |
| Lub Oil Status (Level & Colour)                      | OK    | DG RH Meter Working Properly                  | OK       |
| No Parts Missing (if missing, note in snags below)   | OK    |                                               |          |


### SNAGS FOUND (2)

| SNAG # | SYSTEM | CATEGORY   | COMPONENT                     | STATUS | OBSERVATIONS | ACTION | PHOTO                                                                                 |
|--------|--------|------------|-------------------------------|--------|--------------|--------|---------------------------------------------------------------------------------------|
| S-017  | DG     | DG - Other | DG fan bet losse              | Faulty | —            | Open   |  |
| S-018  | DG     | DG - Other | Radiator s blocked with dust. | Faulty | —            | Open   |  |

### DEFICIENCIES & SAFETY REMARKS

|                       |                                          |
|-----------------------|------------------------------------------|
| DG MAJOR DEFICIENCIES | 1) Fan belt loose 2) Radiator not ciling |
| SAFETY REMARKS        | —                                        |
| GENERAL REMARKS       | —                                        |

SITE PHOTOS



Site / Nameplate



DG RH / Meter



Fuel Gauge

**Md. Eidris Ali**

Handed Over By · Dhaly Infratech  
01750537433

Date: \_\_\_\_\_

**Md. Ismail Hossain**

Taken Over By · Alliance Computers  
Limited  
01847426858

Date: \_\_\_\_\_


BL Concern · Name / Signature

Date: \_\_\_\_\_


## APPENDIX — PHOTO EVIDENCE (5)

Full-size reference photos for SYL\_X0086, grouped by type and numbered for cross-reference against the tables above.

### REQUIRED SITE PHOTOS (3)

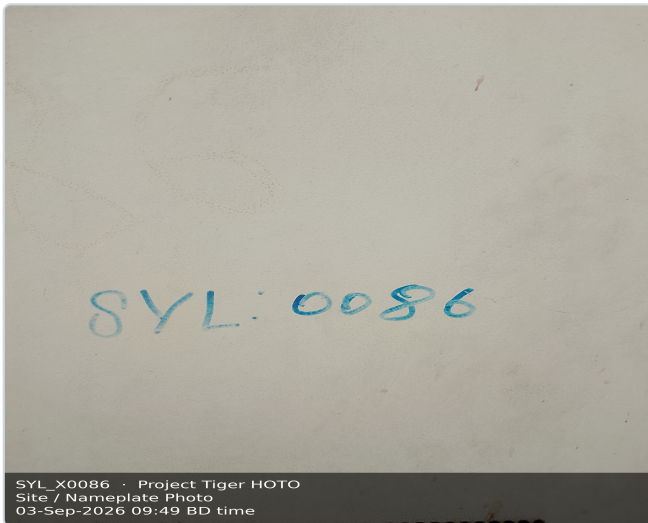

**Photo 1 — Site / Nameplate**

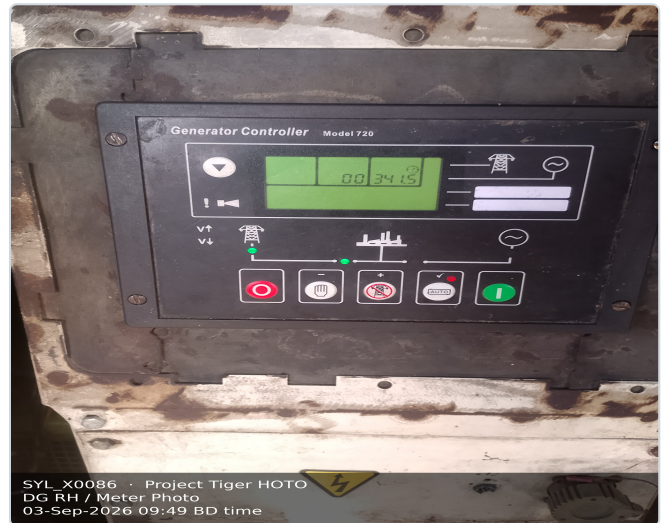


**Photo 2 — DG RH / Meter**



**Photo 3 — Fuel Gauge**

## SNAG EVIDENCE PHOTOS (2)

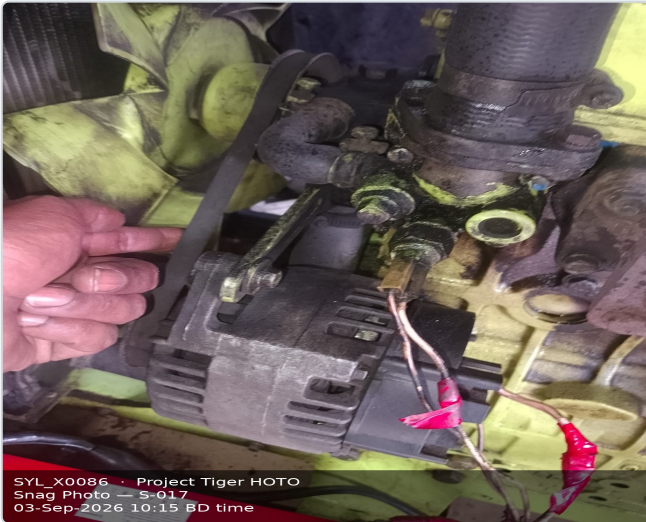

**Photo 4 — S-017 — DG fan bet losse**



**Photo 5 — S-018 — Radiator s blocked with dust.**
