

Site HOTO Report — DHK_X5181

Project Tiger · Dhaly Infratech → Alliance Computers Limited · Generated 07-Sep-2026 20:53 BD time

73%

FORM COMPLETION

15/15

CHECKLIST OK

0

OPEN SNAGS

0

TOTAL SNAGS

8

PHOTOS ATTACHED

Incomplete: the following expected fields were left blank in this submission — Site Type, BTS Type, Site Sharing.

SITE & HANDOVER DETAILS

SITE CODE	DHK_X5181	ZONE	Sylhet
HOTO DATE	2026-09-03	DISTRICT	Narsingdi
HANDOVER ORG	Dhaly Infratech	TAKEOVER ORG	Alliance Computers Limited
HANDOVER PERSON	Md Mahabub	TAKEOVER PERSON	Mir Hossain
HANDOVER PHONE	01615220637	TAKEOVER PHONE	01715163312
INSPECTED BY	Sojib Hossan	SECURITY GUARD	No
ACCESS KEY HANDED OVER	—	SITE TYPE	Not Filled
BTS TYPE	Not Filled		
SHARED WITH OPERATOR	Not Filled	SHARED OPERATOR NAME	—

GENERATOR INFORMATION

DG BRAND	Pramac	GENSET ASSET NO.	—
CAPACITY (KVA)	22	TYPE	—
FUEL TANK CAPACITY	200	PRESENT RH	—
FUEL (NO WATER)	365 L	FUEL (TOTAL)	379 L
WATER AMOUNT	14 L	FUEL AMOUNT (WORD)	Three Hundred Seventy Nine Liters
DG SITE TYPE	—	DG LOCKED AFTER FUELING	Yes
DG PRESENT STATUS	OK	GENSET ON ALARM	—
BATTERY BRAND	—	BATTERY SERIAL	—
BATTERY AH	—	ENGINE SERIAL	—
ATS BRAND	—	ATS MODE	Auto
RH METER TYPE	—	LAST SERVICE DATE	—
KEY TYPE	Local Key	KEY STATUS — BTS	—
KEY STATUS — DG ROOM	Local		

ACTIVE DG	1	CONNECTED FUEL TANKS	1
FAULTY/DISCONNECTED DG	1	FAULTY/DISCONNECTED TANKS	1

CONNECTED GENERATOR CHECKLIST & READINGS

ITEM	VALUE	ITEM	VALUE
Earth Connection OK	Yes	Phase	3 Phase
Voltage L1-N	220	Voltage L2-N	225
Voltage L3-N	229	Current Line 1	-2
N-G	-2	Engine Brand	Pramic
Controller Status	OK	Black Smoke Status	OK
DG Battery Charger	OK	ATS Physical & Functional Status	OK
DG Automation (VDTC/RVDTC/Rectifier) per BL Standard	OK	Fuel Preserved at Safe & Appropriate Location	OK
Exhaust Fan / Ventilation Sufficient When Running	OK	Sufficient Water in Radiator & Battery	OK
DG Radiator Condition	OK	DG Battery Condition	OK
DG Runs in Both Auto & Manual Mode	OK	GENSET ON Alarm Functioning Properly	OK
Lub Oil Status (Level & Colour)	OK	DG RH Meter Working Properly	OK
No Parts Missing (if missing, note in snags below)	OK		

SNAGS FOUND (0)

No snags logged for this visit.

DEFICIENCIES & SAFETY REMARKS

DG MAJOR DEFICIENCIES	1,DG Air Filter Box Lock Missing, 2,Ari Filter Missing 3,Radiator Muntin Broken 4,Out Door BTS Room Light Faulty
SAFETY REMARKS	1,Fire Extinguisher Missing
GENERAL REMARKS	—

SITE PHOTOS

		
Site / Nameplate	DG RH / Meter	Fuel Gauge



Additional



Additional



Additional



Additional



Additional

Md Mahabub

Handed Over By · Dhaly Infratech
01615220637

Date: _____

Mir Hossain

Taken Over By · Alliance Computers
Limited

01715163312

Date: _____

BL Concern · Name / Signature

Date: _____

APPENDIX — PHOTO EVIDENCE (8)

Full-size reference photos for DHK_X5181, grouped by type and numbered for cross-reference against the tables above.

REQUIRED SITE PHOTOS (3)



Photo 1 — Site / Nameplate



Photo 2 — DG RH / Meter



Photo 3 — Fuel Gauge

ADDITIONAL PHOTOS (5)



Photo 4 — Site Context 1

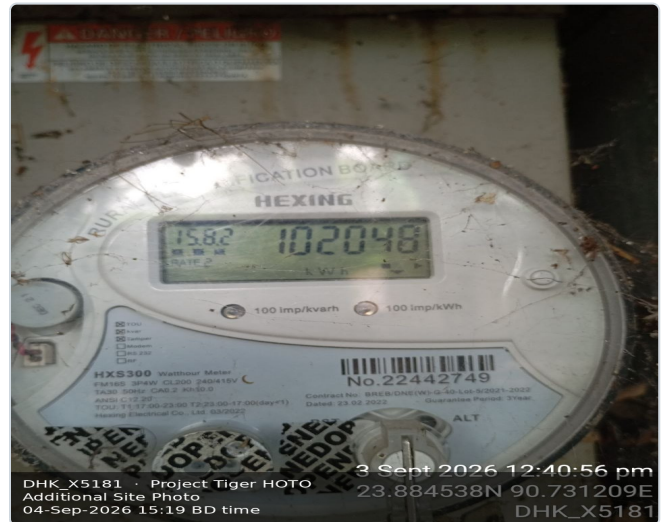


Photo 5 — Site Context 2



Photo 6 — Site Context 3



Photo 7 — Site Context 4



Photo 8 — Site Context 5
